King Hall Photography Remodel | Goebelj Schedule_1 | 19-Jun-07 07:39

Activity ID	Activity Name	Remaining Duration	Schedule % Complete	Start	Finish
DESGN DESIGN & ENGINEERING		14	0%	11-May-07 A	09-Jul-07
Jeff Goebel		14	0%	19-Jun-07	09-Jul-07
A1010	Bid	14	0%	19-Jun-07	09-Jul-07
Jim Nelson		0	0%	04-Jun-07 A	15-Jun-07 A
A1190	Mechanical Design	0	100%	04-Jun-07 A	15-Jun-07 A
Jamie Feeney		0	0%	11-May-07 A	15-Jun-07 A
A1000	Design Work	0	100%	11-May-07 A	15-Jun-07 A
Brian Stitch		0	0%	04-Jun-07 A	15-Jun-07 A
A1200	Electrical Design	0	6.67%	04-Jun-07 A	15-Jun-07 A
CONST CONSTRUCTION		46	0%	15-May-07 A	22-Aug-07
Jeff Goebel		46	0%	19-Jun-07	22-Aug-07
A1030	Start Work	0	0%	19-Jun-07	
A1050	Asbestos removal	10	0%	25-Jun-07*	13-Jul-07
A1110	Order Casework	35	0%	19-Jun-07	07-Aug-07
A1210	Finished	0	0%		22-Aug-07
A1240	Order Doors & Hardware	20	0%	19-Jun-07	17-Jul-07
Brad Goeller		46	0%	15-May-07 A	22-Aug-07
A1020	Construction	20	0%	16-Jul-07	10-Aug-07
A1040	Demo	0	100%	15-May-07 A	17-May-07 A
A1060	Frame walls	3	0%	19-Jun-07	21-Jun-07
A1090	Sheet rock & taping	5	0%	24-Jul-07	30-Jul-07
A1150	Set Sinks	1	0%	14-Aug-07	14-Aug-07
A1180	Equipment Installation	2	0%	21-Aug-07	22-Aug-07
A1250	Door - stain & finish	2	0%	18-Jul-07	19-Jul-07
A1260	Door - Installation	2	0%	20-Jul-07	23-Jul-07
A1270	Hardware Installation	2	0%	24-Jul-07	25-Jul-07
A1290	Painting	3	0%	31-Jul-07	02-Aug-07
Jim Williamson		2	0%	20-Jul-07	23-Jul-07
A1220	Phone & Data Cable	2	0%	20-Jul-07	23-Jul-07
No Responsibility		30	0%	10-Jul-07	20-Aug-07
A1070	Electrical Rough in	8	0%	10-Jul-07	19-Jul-07
A1080	Mechanical Rough in	8	0%	10-Jul-07	19-Jul-07
A1100	Casework installation	4	0%	08-Aug-07	13-Aug-07
A1120	Install cieling grid	2	0%	31-Jul-07	01-Aug-07
A1130	Install lighting	3	0%	02-Aug-07	06-Aug-07
A1140	Mechanical finish	5	0%	31-Jul-07	06-Aug-07
A1160	Ceiling tiles	2	0%	07-Aug-07	08-Aug-07
A1170	Flooring installation	3	0%	14-Aug-07	16-Aug-07
A1230	Card access installation	3	0%	24-Jul-07	26-Jul-07
A1280	Electrical Finish	5	0%	14-Aug-07	20-Aug-07

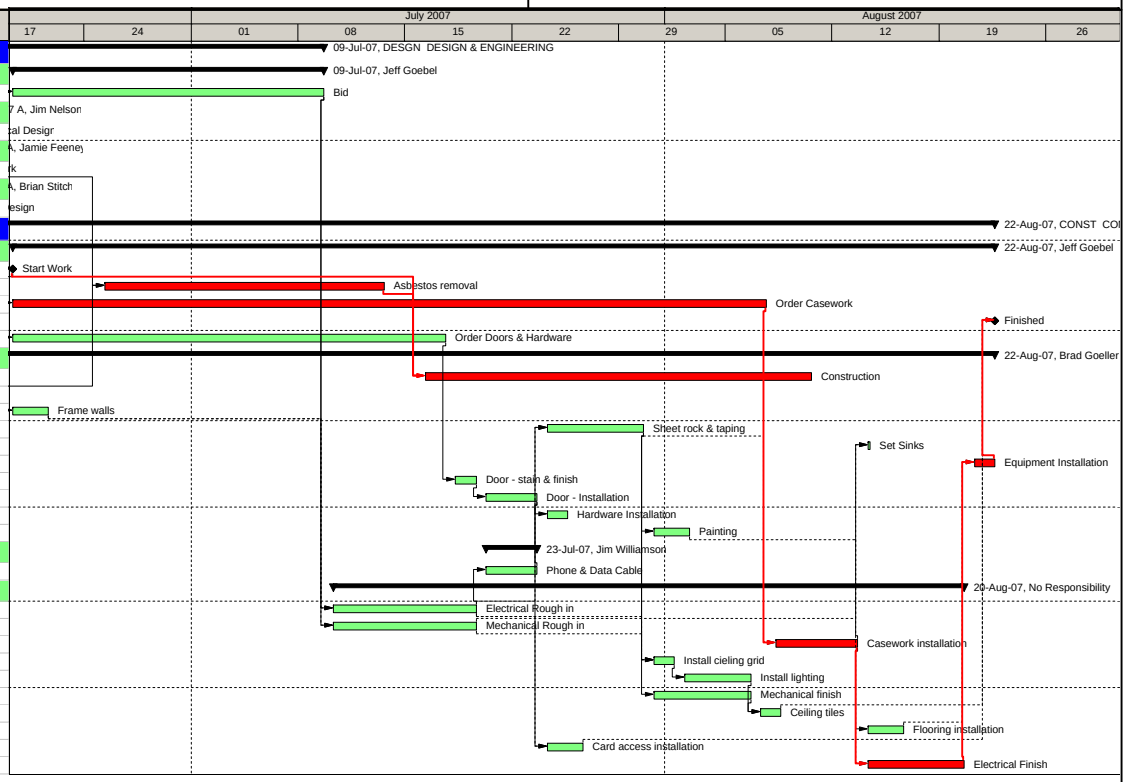

Actual Work | Critical Remainin...
Remaining Work | ◆◆ Milestone

TASK filter: All Activities

(c) Primavera Systems, Inc.
